

Smb Jan 28, 2017

Work Order ID 154713

154713

Page 1

Monday, December 19, 2016 4:14:40 PM

Item ID: D4634-141 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Fwd, Center Ceiling Replacement Panel Assembly
 Start Date: 1/9/2017 Start Qty: 1.00 *1* Cust Item ID:
 Required Date: 1/13/2017 Req'd Qty: 1.00 *1* Customer:
 Reference:

Approvals: Process Plan: DAS 21 9-89 Date: DEC 20 2016 Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D4634	G

100		0.00							
100									
HandThermo	Memo	0.14							
Hand Finishing Thermoforming	Pick Kit								

JAN 12 2017

DAS
6
9-89

110		0.00							
110									
Small Fab	Memo	0.21							
Small Fab	Assemble as per Dwg D4634-141								

Smb
17/1/23

1- Scuff bonding surface to eliminate in-perfections and increase bonding and clean with wash& wipe

2- Locate and glue down Channel Assy, angles, brackets, and mounting pads using 3M Plastic welder II.

Batch # 135436Expiry Date Feb 2017

3- Apply labels as per Dwg. and seal with 3M 3950 edge sealer

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition			
				Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

Work Order ID 154713

Monday, December 19, 2016 4:14:40 PM

154713

Page 2

Item ID: D4634-141 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Fwd, Center Ceiling Replacement Panel Assembly
Start Date: 1/9/2017 Start Qty: 1.00 ***1*** Cust Item ID:
Required Date: 1/13/2017 Req'd Qty: 1.00 ***1*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
125	QC5- Inspect part completeness to step on W/O	0.00							
125									
QC	Memo	0.00				①	12.0.23		DAS 9 9-89
Quality Control									
130	Identify as per dwg & Stock Location: _____	0.00							
130									
Packaging	Memo	0.00							SMB 17/1/24
Packaging									
140	QC21- Final Inspection - Work Order Release	0.00							
140									
QC	Memo	0.02							DAS 21 9-89
Quality Control									JAN 2 6 2017

DAS
21
9-89

JAN 2 6 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐				
Date :	Step #:	QTY Effective :			MRB (QS1042) Approval	
Description Work Order Deviation		Disposition			Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐				
		OTHER : ☐				

Picklist Print

Monday, December 19, 2016 4:14:45 PM

Page 1

Work Order ID: 154713

154713

Parent Item: D4634-141

D4634-141

Parent Item Name: Fwd, Center Ceiling Replacement Panel Assembly

Start Date: 1/9/2017

Required Date: 1/13/2017

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP Rev. A 12/08/09 New Issue DL
 12/11/08 Document release DL VERIFIED BY:JLM
 Dwg Update DL verf: DD
 DL
 DL
 DL
 DL
 IPP Rev B
 IPP Rev C 13/07/09
 IPP Rev D Dwg Update 13/12/23
 IPP REV E Dwg update 14/01/09
 IPP Rev F Dwg. update 14/02/03
 IPP Rev G Dwg. Update 15/01/27

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

D5021-1

Manufactured

No

100

Each

2.0000

1

1

D5021-1

Foam, Center Panel, Fwd

**

JAN 12 2017

DAS
6
9-89

Location

Loc Qty

Loc Code

MF010

2

123921

2

MS20426AD3-4

Purchased

No

100

Each

8,977.000

4

4

MS20426AD3-4

RIVET

**

JAN 12 2017

DAS
6
9-89

Location

Loc Qty

Loc Code

CCK004

4885

m136444

4885

GA

5

m131697

5

ST312

4087

m134204

4087

m136180

4

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QS1042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		

Root Cause				FAULT CATEGORY			
Environment ☐	☐ No Re-verification	Pressure/Forced ☐	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong		
Design ☐	☐ Operator	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐		
Doc/Data ☐	☐ Offset/Setup	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐		
Equip/Tooling ☐	☐ Supplier	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐		
Handling/Pre ☐	☐ Training	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐		
Material ☐	☐ Use for Testing	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐		
Internal Transport ☐	☐ Poor Information	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐		
Tribal Knowledge ☐	☐ Rushing	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐		
LOA ☐	☐ Product Improvement	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐		
Substation ☐	☐ Process Improvement	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐		
Past Expiry Date ☐	☐ Manufacturing Process	OTHER : ☐					
Misidentified ☐	☐ Past Due						

Picklist Print

Monday, December 19, 2016 4:14:45 PM

Work Order ID: 154713

154713

Parent Item: D4634-141

D4634-141

Parent Item Name: Fwd, Center Ceiling Replacement Panel Assembly

Start Date: 1/9/2017

Required Date: 1/13/2017

Start Qty: 1.00

Required Qty: 1.00

MS20426AD4-6

Purchased

No

100

Each

675.0000

2

2

MS20426AD4-6

Rivet

**

JAN 12 2017

DAS
6
9-89

Location

Loc Qty

Loc Code

GA

85

M134502

85

ST311

590

M134502

590

MS21059L08

Purchased

No

100

Each

103.0000

2

2

JAN 12 2017

MS21059L08

Nut

**

DAS
6
9-89

Location

Loc Qty

Loc Code

ST300

103

m134634

3

m134943

100

D4634-1

Manufactured

No

100

Each

0.0000

1

1

D4634-1

Fwd, Center Ceiling Panel

**

D154715 SMB

D4636-5

Manufactured

No

100

Each

41.0000

1

1

D4636-5

Bracket

**

JAN 12 2017

DAS
6
9-89

Location

Loc Qty

Loc Code

ST115

41

149102

41

D4647-5

Manufactured

No

100

Each

9.0000

1

1

D4647-5

Doubler

**

JAN 12 2017

DAS
6
9

Location

Loc Qty

Loc Code

MF004

9

125019

1

129252

8

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QS1042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____	
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

Picklist Print

Monday, December 19, 2016 4:14:45 PM

Page 3

Work Order ID: 154713

154713

Parent Item: D4634-141

D4634-141

Parent Item Name: Fwd, Center Ceiling Replacement Panel Assembly

Start Date: 1/9/2017

Required Date: 1/13/2017

Start Qty: 1.00

Required Qty: 1.00

D4664-5

Manufactured No

100

Each

31.0000

6

6

D4664-5

Spacer

5X B: 154825

**

JAN 12 2017

DAS
6
9-89

Location

Loc Qty

Loc Code

MF004

31

149152

31

D4712-1

Manufactured No

100

Each

18.0000

1

1

D4712-1

Bracket

**

JAN 12 2017

DAS
6
9-89

Location

Loc Qty

Loc Code

MF004

18

125020

7

149103

11

D4732-15

Manufactured No

100

Each

3.0000

1

1

D4732-15

Label

**

JAN 12 2017

DAS
6
9-89

Location

Loc Qty

Loc Code

MF005

3

149086

3

D4732-19

Manufactured No

100

Each

9.0000

1

1

D4732-19

Label

**

JAN 12 2017

DAS
6
9-89

Location

Loc Qty

Loc Code

MF005

9

123209

9

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By 	
								Lead hand / Supervisor Approval Verification 	
								QC / QA Coordinator Approval 	

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER : _____							
Misidentified	☐	Past Due	☐								

Picklist Print

Monday, December 19, 2016 4:14:45 PM

Work Order ID: 154713

154713

Parent Item: D4634-141

D4634-141

Parent Item Name: Fwd, Center Ceiling Replacement Panel Assembly

Start Date: 1/9/2017

Required Date: 1/13/2017

Start Qty: 1.00

Required Qty: 1.00

MPNY-750S-9-C

Purchased

No

100

Each

747.0000

7

7

MPNY-750S-9-C

Mounting Pad

Location

Loc Qty

Loc Code

ST569

747

M130423

747

JAN 12 2017

DAS

7

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step # : _____		QTY Effective : _____			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By _____		
							Lead hand / Supervisor Approval Verification _____		
							QC / QA Coordinator Approval _____		

Root Cause			FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence
Past Expiry Date	☐	Manufacturing Process	☐	OTHER : 						
Misidentified	☐	Past Due	☐							

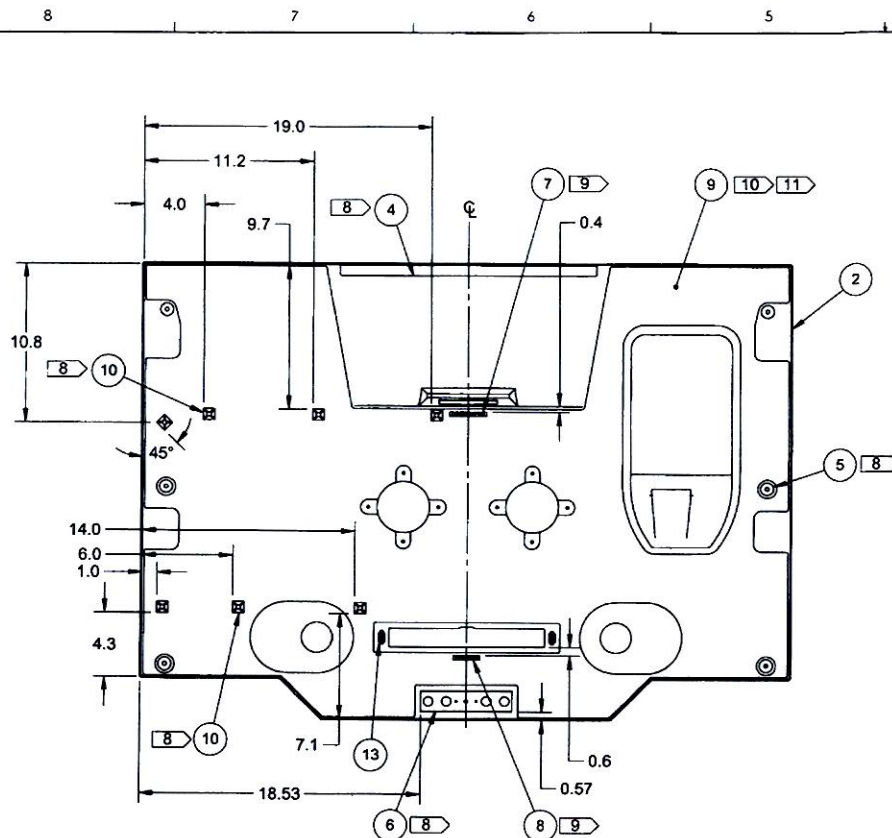


D4634-141 FWD, CENTER CEILING REPLACEMENT PANEL ASSY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: N/A
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: N/A
- 8) APPLY A BEAD (0.20 TO 0.30 WIDE) OF DEVCON PLASTIC WELDER II (0.25 INSIDE OF BOTH EDGES OF PART) TO BOND D4664-5, D4712-1 & MPNY-750S-9C. WAIT FOR 2 TO 4 HOURS FOR FUNCTIONAL CURE.
- 9) LOCATE LABELS AS SHOWN. SEAL LABELS USING 3950 EDGE SEALER OVER LABEL TOP SURFACE
- 10) APPLY AN EVEN COAT OF 3M SCOTCH WELD 1300L CONTACT ADHESIVE TO BOND D5021-1 FOAM CORE TO INSIDE OF PANEL
- 11) CENTER D5021-1 FOAM ON D4634-1

ITEM	QTY -141	P/N	DESCRIPTION
1	X	D4634-141	FWD, CENTER CEILING REPLACEMENT PANEL ASSY
2	1	D4634-1	FWD, CENTER CEILING PANEL
3	1	D4636-5	BRACKET
4	1	D4647-5	DOUBLER
5	6	D4664-5	SPACER
6	1	D4712-1	BRACKET
7	1	D4732-15	LABEL
8	1	D4732-19	LABEL
9	1	D5021-1	FOAM, CENTER PANEL, FWD
10	7	MPNY-750S-9-C	MOUNTING PAD
11	4	MS20426AD3-(4)	RIVET, SOLID, CSK
12	2	MS20426AD4-(6)	RIVET, SOLID, CSK
13	2	MS21059L08	NUT PLATE

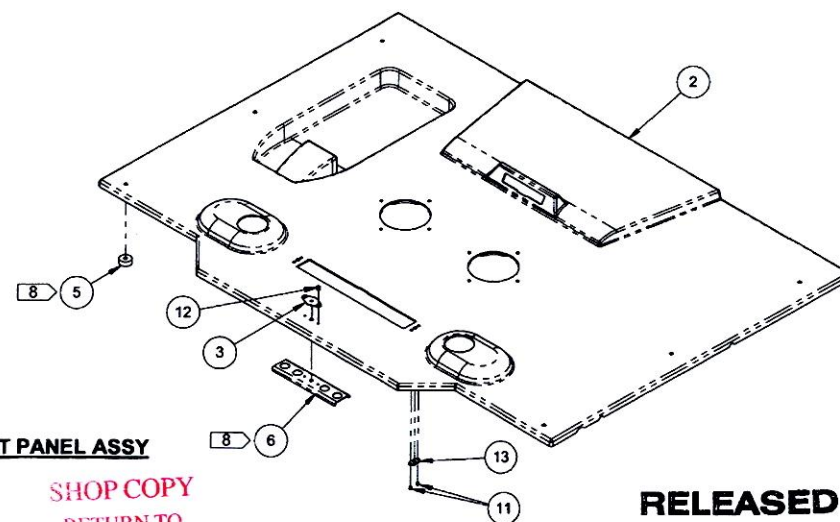

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 154713
MCS
1612-20

RELEASED
2015 JAN 26

DESIGN	RF	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	RF		
CHECKED	AK	DRAWING NO. D4634	REV. G
MFG. APPR.	DL	TITLE CENTER CEILING PANELS	SHEET 7 OF 17
APPROVED	HS		SCALE
DE APPR.	DS		NTS
DATE	14.11.28	COPYRIGHT © 2012 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	
